State of Good Repair (SGR) Program - Summary Master Program Schedule

18-May-25 19:16

Activity ID	Activity Name	Start	Finish
State of Good Repair (SGR) Program		01-Jan-19 A	18-Jul-31
Package 1A		01-Jan-19 A	28-Feb-29
1134245 Bellevue Base Bus Lift Replacement		01-Jan-19 A	19-Jun-26
1134245.P1	Phase 1 - Project Planning	01-Jan-19 A	12-Jun-24 A
1134245.P2	Phase 2 - Preliminary Design	04-Oct-24 A	30-Sep-25
1134245.P3	Phase 3 - Final Design	01-Oct-25	15-Jan-26
1134245.P4	Phase 4 - Implementation	18-Aug-25	24-Mar-26
1134245.P5	Phase 5 - Closeout	25-Mar-26	19-Jun-26
1139350 Bellevue Base Vehicle Maintenance Bus Lift Replacement		23-Jan-24 A	20-Sep-28
1139350.P1	Phase 1 - Project Planning	23-Jan-24 A	19-Aug-24 A
1139350.P2	Phase 2 - Preliminary Design	23-Jan-24 A	31-Mar-27
1139350.P3	Phase 3 - Final Design	10-Oct-24 A	22-Oct-27
1139350.P4	Phase 4 - Implementation	25-Oct-27	21-Aug-28
1139350.P5	Phase 5 - Closeout	05-Apr-28	20-Sep-28
1134246 TDC Atlantic Base Bus Lift Replacement		02-Jan-19 A	28-Feb-29
1134246.P1	Phase 1 - Project Planning	02-Jan-19 A	29-Oct-20 A
1134246.P2	Phase 2 - Preliminary Design	26-Oct-20 A	26-Sep-24 A
1134246.P3	Phase 3 - Final Design	23-Jan-24 A	26-Mar-27
1134246.P4	Phase 4 - Implementation	22-Jan-27	06-Oct-28
1134246.P5	Phase 5 - Closeout	25-Aug-28	28-Feb-29
Package 2A		04-Jan-21 A	18-Jul-31
1134269 South Base Fluid UST's		04-Jan-21 A	18-Jul-31
1134269.P1	Phase 1 - Project Planning	04-Jan-21 A	07-May-25
1134269.P2	Phase 2 - Preliminary Design	08-May-25	06-Dec-27
1134269.P3	Phase 3 - Final Design	07-Dec-27	25-Mar-30
1134269.P4	Phase 4 - Implementation	10-Dec-29	24-Mar-31
1134269.P5	Phase 5 - Closeout	25-Mar-31	18-Jul-31
Package 3A		06-Jun-24 A	06-Feb-29
1134377 All Transit Bases Overall Fire System Replacement 2023-2024		07-Jun-24 A	12-Jul-27
1134377.P1	Phase 1 - Project Planning	07-Jun-24 A	08-Jul-25
1134377.P4	Phase 4 - Design & Implementation	11-Sep-24 A	04-May-27
1134377.P5	Phase 5 - Closeout	05-May-27	12-Jul-27
1144094 Ryerson Base Operations Sewer piping Replace		10-Jun-24 A	17-Jul-28
1144094.P1	Phase 1 - Project Planning	10-Jun-24 A	08-Jul-25
1144094.P2	Phase 2 - Preliminary Design	09-Sep-24 A	30-Mar-26
1144094.P3	Phase 3 - Final Design	09-Mar-26	13-Aug-27
1144094.P4	Phase 4 - Implementation	16-Aug-27	22-May-28
1144094.P5	Phase 5 - Closeout	23-May-28	17-Jul-28
1144092 OA IWS System Replacement		10-Jun-24 A	01-Sep-28
1144092.P1	Phase 1 - Project Planning	10-Jun-24 A	08-Jul-25
1144092.P2	Phase 2 - Preliminary Design	03-Sep-24 A	25-Mar-26
1144092.P3	Phase 3 - Final Design	11-Mar-26	13-Aug-27
1144092.P4	Phase 4 - Implementation	16-Aug-27	14-Jul-28
1144092.P5	Phase 5 - Closeout	10-Jul-28	01-Sep-28
1134331 Countywide Routine Equip Replacement		06-Jun-24 A	06-Feb-29
1134331.P1	Phase 1 - Project Planning	06-Jun-24 A	08-Jul-25
1134331.P4	Phase 4 - Design & Implementation	09-Jul-25	14-Dec-28
1134331.P5	Phase 5 - Closeout	08-Dec-28	06-Feb-29
1144126 Overall P&R SGR 2023-2024		10-Jun-24 A	06-Jun-28
1144126.P1	Phase 1 - Project Planning	10-Jun-24 A	08-Jul-25
1144126.P4	Phase 4 - Design & Implementation	12-Sep-24 A	17-Apr-28
1144126.P5	Phase 5 - Closeout	18-Apr-28	06-Jun-28
Package 6		24-Jul-24 A	15-Feb-30
1134242 South Base OM HVAC Replacement		24-Jul-24 A	15-Feb-30
1134242.P1	Phase 1 - Project Planning	24-Jul-24 A	26-Jan-26
1134242.P2	Phase 2 - Preliminary Design	24-Jul-24 A	05-Jan-27
1134242.P3	Phase 3 - Final Design	05-Oct-26	02-Sep-27
1134242.P4	Phase 4 - Implementation	26-Mar-27	08-Oct-29
1134242.P5	Phase 5 - Closeout	17-Jul-29	15-Feb-30

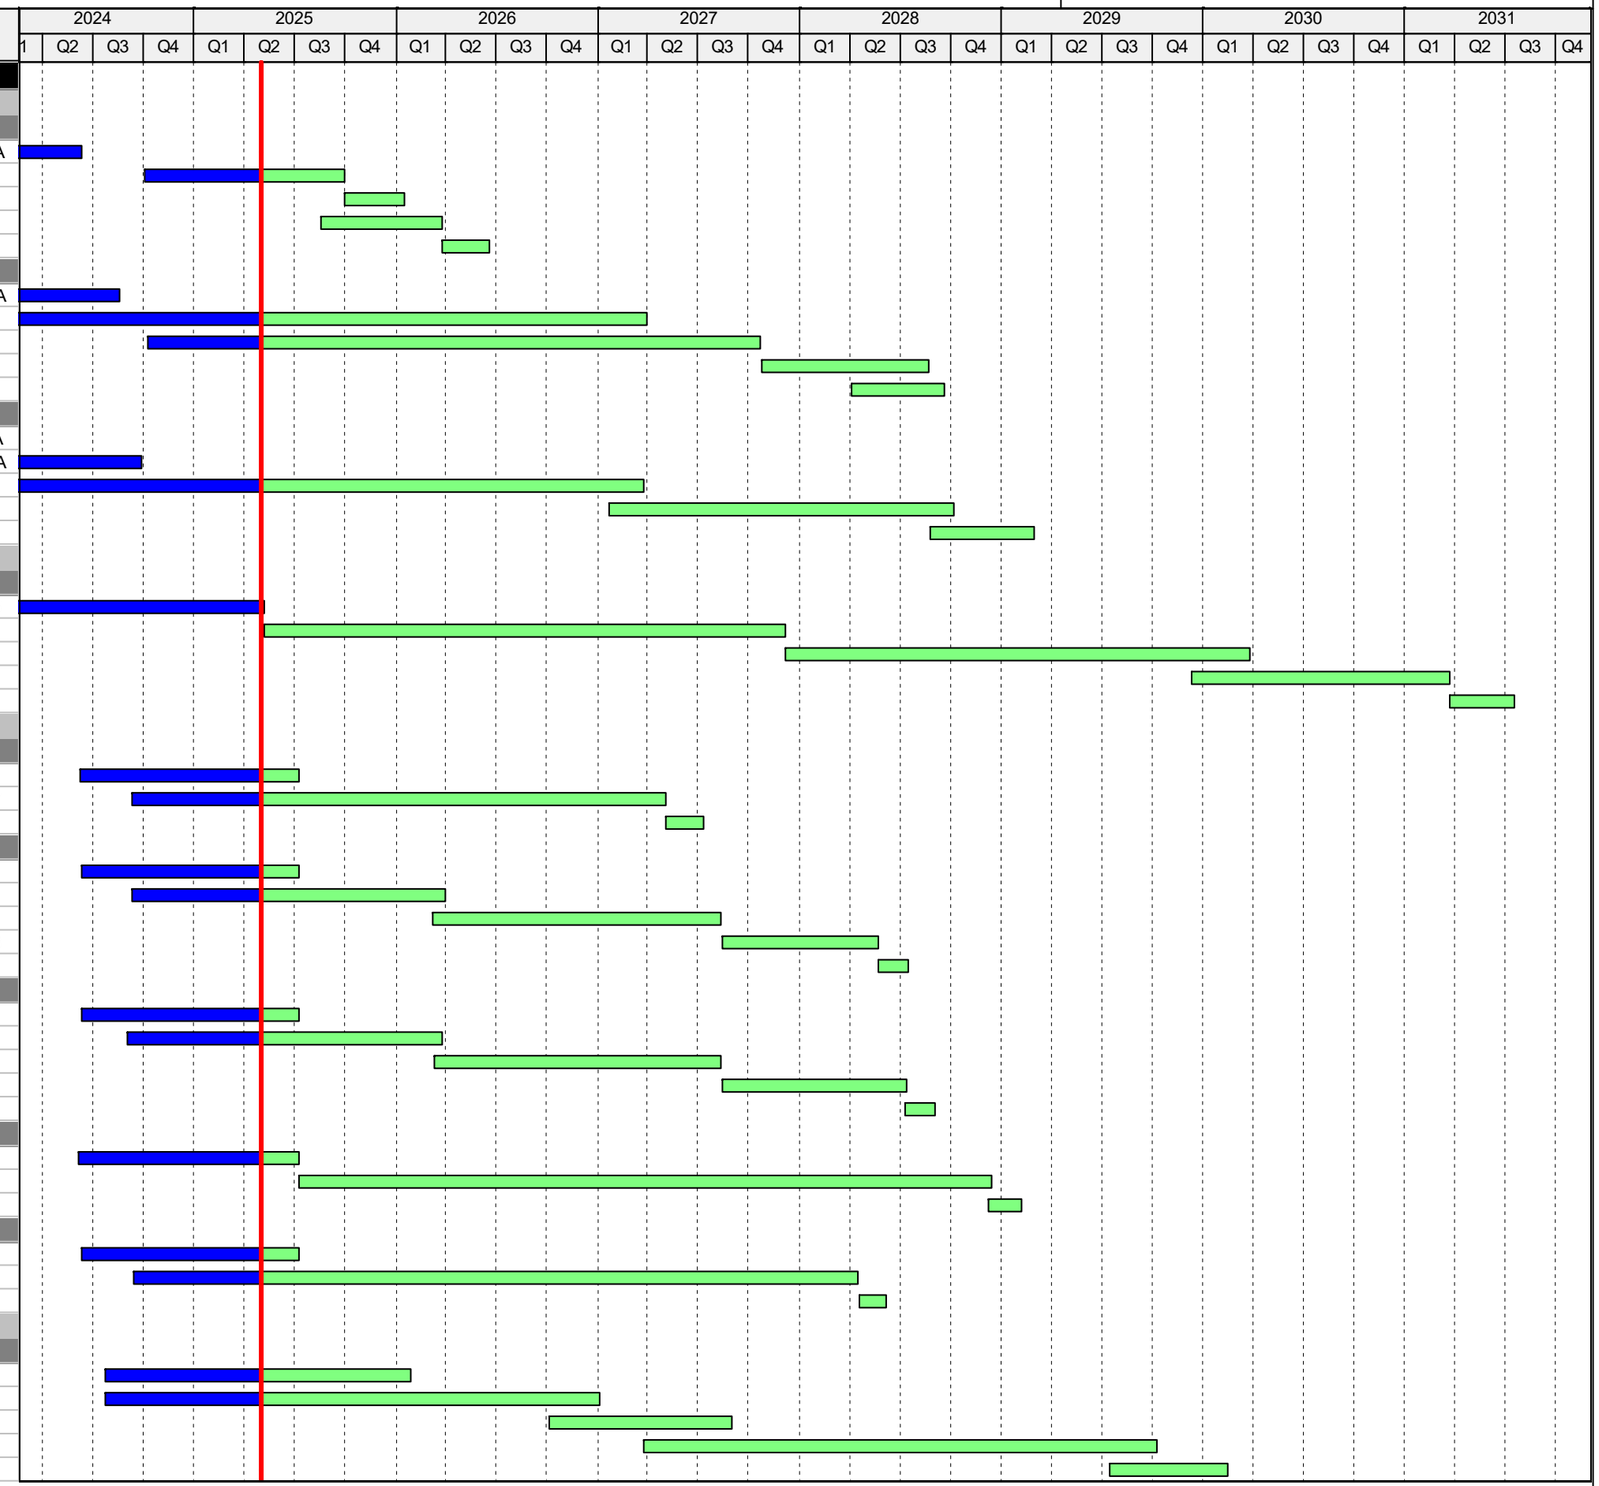

Actual Work | Remaining Work | Critical Remaining Work | ◆ Mi...

TASK filter: (Untitled Filter).
